

GRAVELINE BAY MARSH CREATION PROJECT CONSTRUCTION UPDATE




NOVEMBER 2022




- Contractor's dredge was out-of-service for 6 weeks. Construction recommenced in October 2022.
- 23 of the 55 mounds have been created to date (10/28/2022).
- The mounds will be planted once they are all constructed. Oyster shell will be placed on the northern large mounds.
- The contractor has 270 days to finish the project which would be in February 2023. The contractor is on track to meet the schedule.

PROGRESS MAP

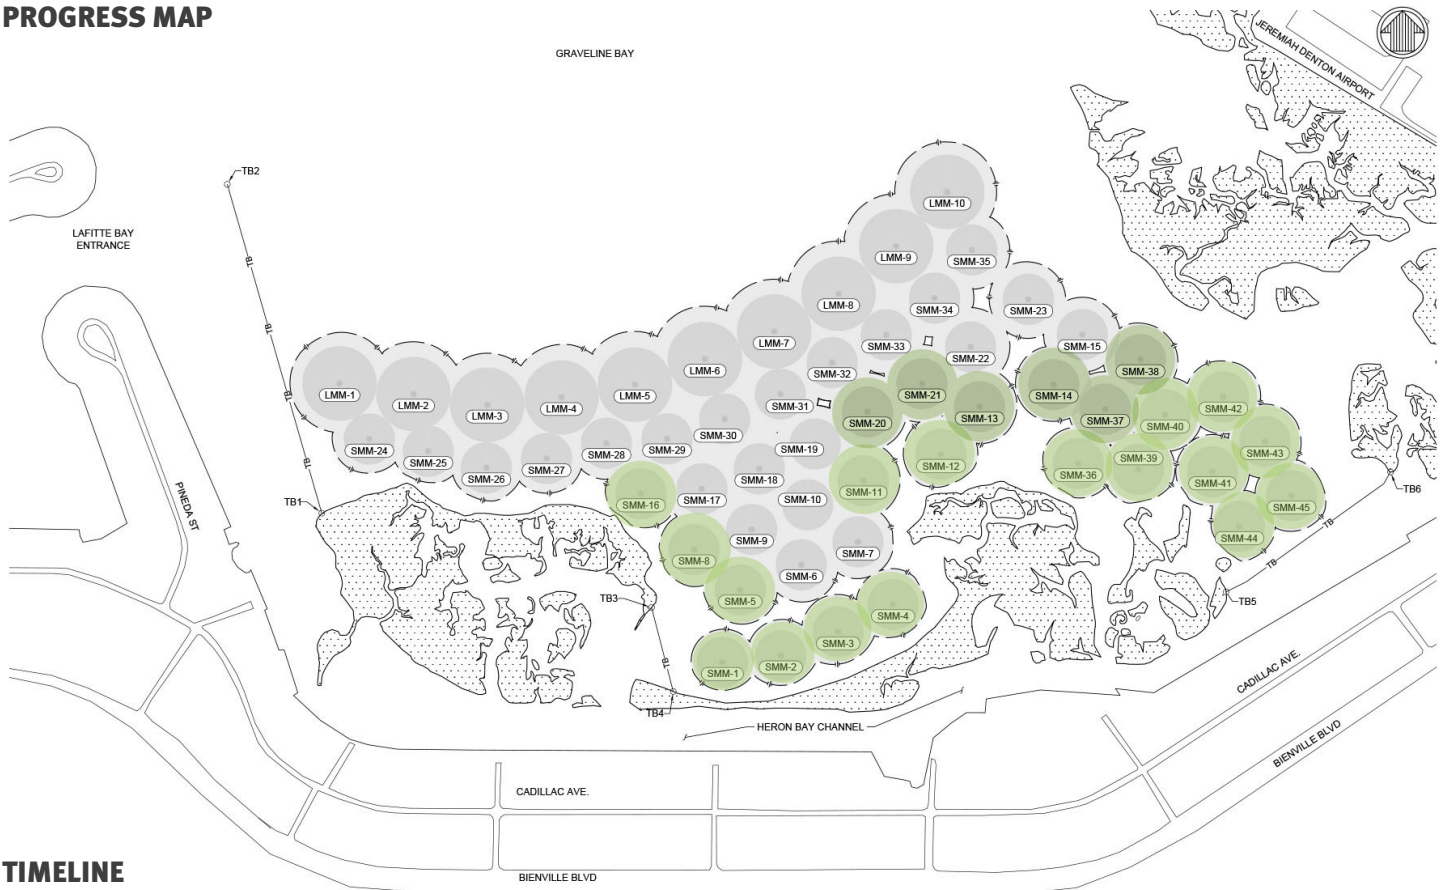

TIMELINE



Contact: Town of Dauphin Island, 1011 Bienville Blvd, Dauphin Island, AL 36528 | Tel: 251-861-5525
